



Left Plot w/ Pics








505-341-0109

| | | | | | |
|-----------------------------------|----------------------------------|-------------------------------------|--------------------------------------|--------------|---------------------------------------|
| Pipe ID L8-11 | City | Street LINCOLN CIR 4155 S | Shape | Map #1 | Basin |
| US Manhole L8-11 | Section Length 67.309 | Year Laid | Material CON | Section Type | |
| DS Manhole L8-10 | Inspected Length 240.8 | Year Renewed | Depth US 9 | Depth DS | Joint Leng... Diameter 8 |
| Cleaned | Situation | | Reason | | |
| Date 20160426 | Clean Date | Weather | | Remark | |
| Start Time 13:54 | | | | | |
| Operator MIKE | Customer | Truck 4165 | Inspection Dir. DOWNSTREAM | Info | |
| Operator Comment | P.O. Number | Present | Flow Control | Camera | |



L8-11

Distance: Pos: Val 1 / 2 : % : Gallons:


| | | | | | | | | |
|---|------------|-----------|---|--|--|--|--|--|
|  | Code: TIBU | 0.0 ft. | | | | | | |
| Observation: Inspection Begins at Upstream MH | | | | | | | | |
| Remarks: | | | | | | | | |
|  | Code: CLV | 16.2 ft. | 9 | | | | | |
| Observation: Lateral Active | | | | | | | | |
| Remarks: | | | | | | | | |
|  | Code: CLC | 19.4 ft. | 3 | | | | | |
| Observation: Lateral Capped | | | | | | | | |
| Remarks: | | | | | | | | |
|  | Code: CLV | 42.9 ft. | 3 | | | | | |
| Observation: Lateral Active | | | | | | | | |
| Remarks: | | | | | | | | |
|  | Code: CLV | 120.8 ft. | 3 | | | | | |
| Observation: Lateral Active | | | | | | | | |
| Remarks: | | | | | | | | |
|  | Code: CLC | 133.2 ft. | 9 | | | | | |
| Observation: Lateral Capped | | | | | | | | |
| Remarks: | | | | | | | | |
|  | Code: CLV | 192.8 ft. | 9 | | | | | |
| Observation: Lateral Active | | | | | | | | |
| Remarks: | | | | | | | | |




Left Plot w/ Pics

505-341-0109


| | | | | | |
|-----------------------------------|----------------------------------|-------------------------------------|--------------------------------------|--------------|---------------------------------------|
| Pipe ID L8-11 | City | Street LINCOLN CIR 4155 S | Shape | Map #1 | Basin |
| US Manhole L8-11 | Section Length 67.309 | Year Laid | Material CON | Section Type | |
| DS Manhole L8-10 | Inspected Length 240.8 | Year Renewed | Depth US 9 | Depth DS | Joint Leng... Diameter 8 |
| Cleaned | Situation | | Reason | | |
| Date 20160426 | Clean Date | Weather | | Remark | |
| Start Time 13:54 | | | | | |
| Operator MIKE | Customer | Truck 4165 | Inspection Dir. DOWNSTREAM | Info | |
| Operator Comment | P.O. Number | Present | Flow Control | Camera | |



| | | | | | |
|-----------------------------|-----------|---|--|--|--|
| Code: CLV | 194.8 ft. | 9 | | | |
| Observation: Lateral Active | | | | | |
| Remarks: | | | | | |



| | | | | | |
|------------------------------------|-----------|---------|--|--|--|
| Code: YCC | 237.3 ft. | 12 - 12 | | | |
| Observation: Crack Circumferential | | | | | |
| Remarks: | | | | | |



| | | | | | |
|--|-----------|--|--|--|--|
| Code: TIED | 240.8 ft. | | | | |
| Observation: nspection Ends at Downstream MH | | | | | |
| Remarks: | | | | | |

L8-10




Scaled Plot

505-341-0109

| | | | | | |
|-----------------------------------|----------------------------------|-------------------------------------|------------------------|--------------|---------------------------------------|
| Pipe ID L8-11 | City | Street LINCOLN CIR 4155 S | Shape | Map #1 | Basin |
| US Manhole L8-11 | Section Length 67.309 | Year Laid | Material CON | Section Type | |
| DS Manhole L8-10 | Inspected Length 240.8 | Year Renewed | Depth US 9 | Depth DS | Joint Leng... Diameter 8 |

| | | | | | |
|----------------------------|-------------|----------------------|--------------------------------------|--------|--|
| Cleansed | | Situation | | Reason | |
| Date 20160426 | Clean Date | Weather | | Remark | |
| Start Time 13:54 | | Truck 4165 | Inspection Dir. DOWNSTREAM | Info | |
| Operator MIKE | Customer | Present | Flow Control | Camera | |
| Operator Comment | P.O. Number | | | | |

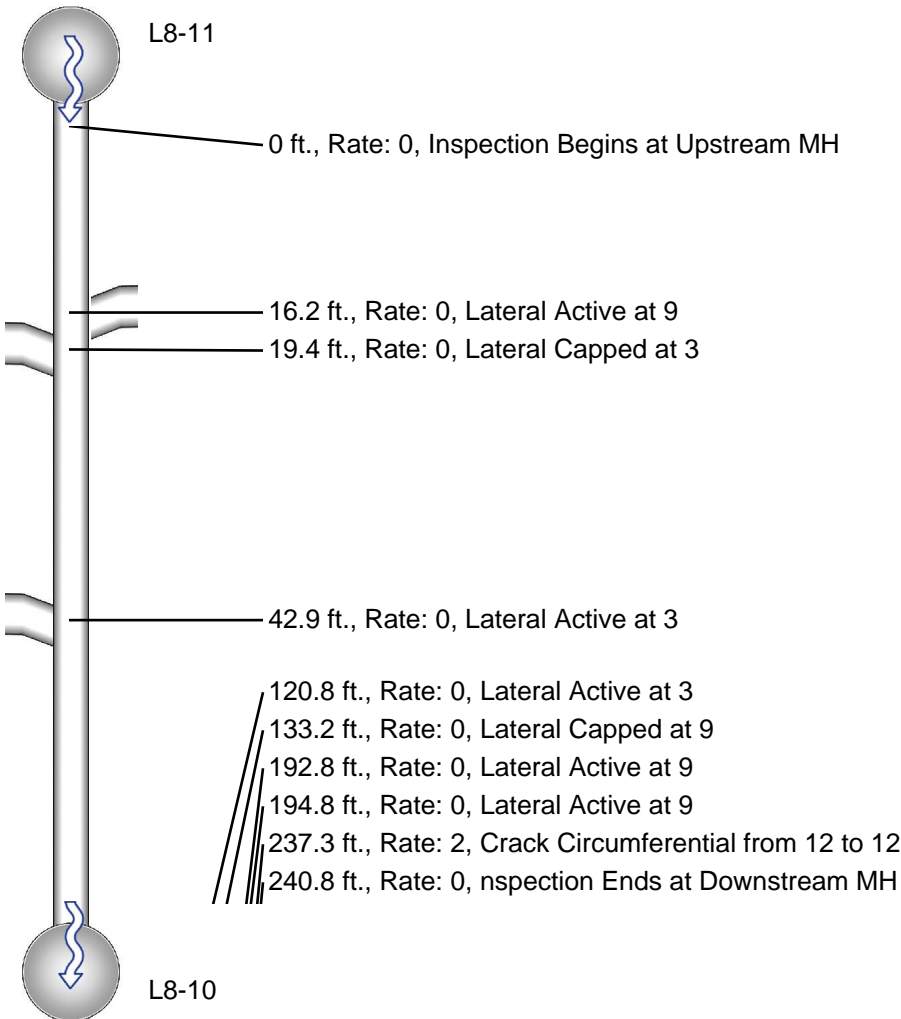

* = clock positions adjusted automatically for reverse inspection

Scale: 1:200
